


LOCUS MAP






CONSTRUCTION SEQUENCE

1. LIMIT OF WORK TO BE STAKE AND SILT FENCE AND HAYBALES TO BE INSTALLED PRIOR TO START OF CONSTRUCTION. EROSION CONTROL TO BE CHECKED BY DESIGN ENGINEER.
2. EXISTING TREES TO BE CLEARED. TREES TO REMAIN SHALL BE PROTECTED DURING CONSTRUCTION WITH SILT FENCE INSTALLED AROUND THE TREES.
3. EXISTING HOUSE TO BE RAZED AND REMOVED FROM SITE.
4. NATURAL STONE WALL & RECHARGE AREA TO BE INSTALLED AND GRADED AND LOAMED & SEEDED.
5. RAIN GARDEN AREA TO BE GRADED AND PLANTED WITH NATIVE PLANTS. SEE LIST.
6. FOUNDATION TO BE STAKED AND INSTALLED. STOCKPILE OF MATERIAL TO BE STORED IN FRONT OF SITE SEE LOCATION ON PLAN.
7. GRADING AROUND FOUNDATION TO BE PERFORMED.
9. HOUSE TO SET ON TOP OF FOUNDATION.
10. SEPTIC SYSTEM TO BE INSTALLED AND COVERED.
11. AS-BUILT TO BE PERFORMED AND SUBMITTED AFTER TWO GROWING SEASONS TO CONSERVATION FOR APPROVAL.

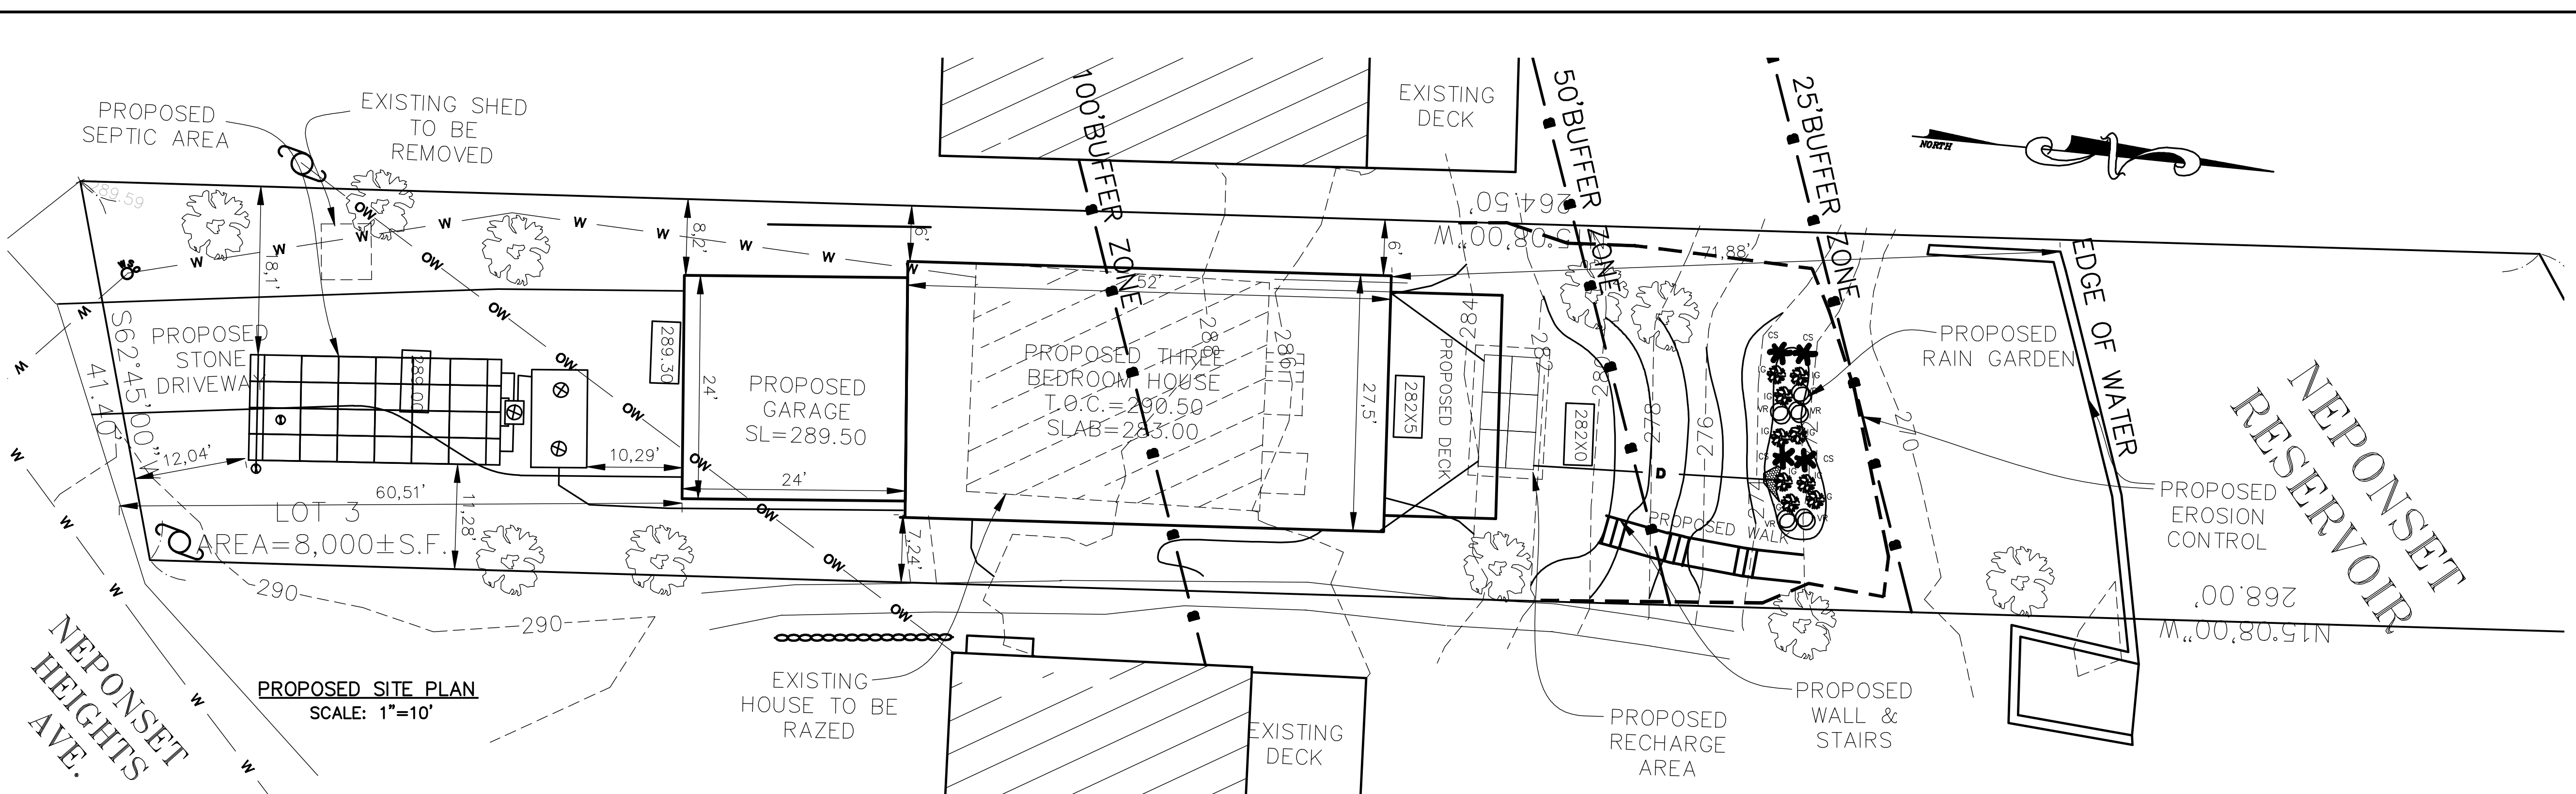

IMPERVIOUS MATERIAL TABLE



QUANTITY	EXISTING	PROPOSED
HOUSE	776 S.F.	2,006 S.F.
DRIVEWAY WALK/PATIO	1,460 S.F.	PROPOSED STONE DRIVEWAY
TOTAL IMPERVIOUS	2,360 S.F.	

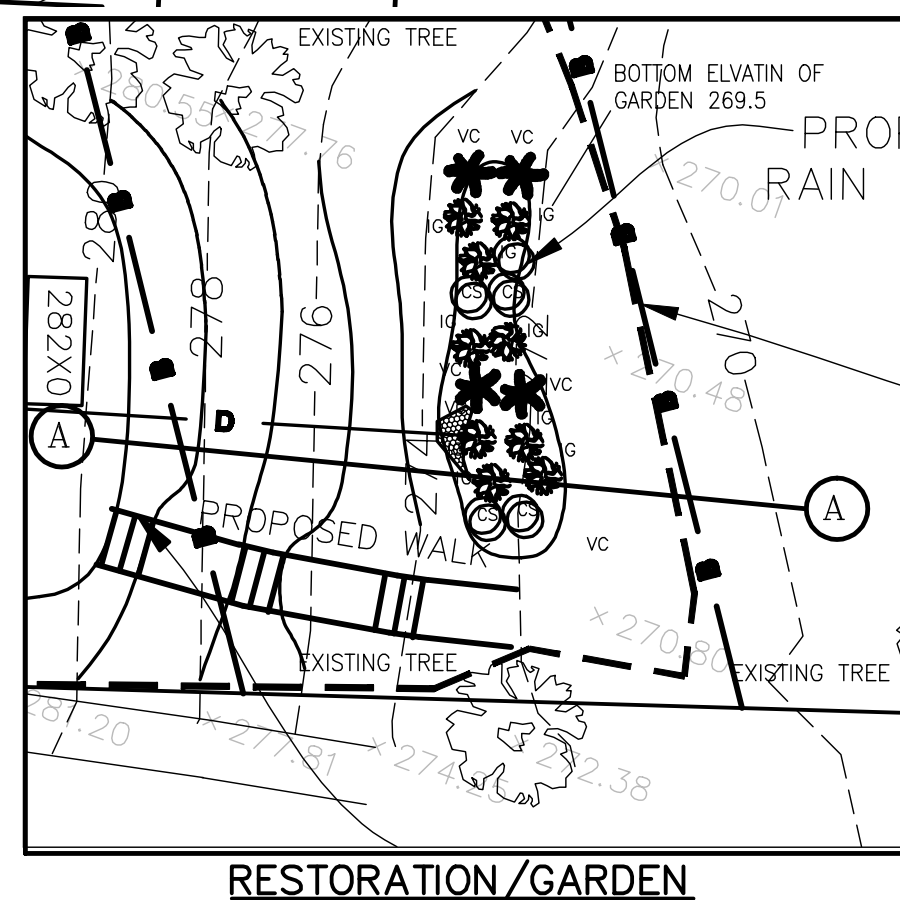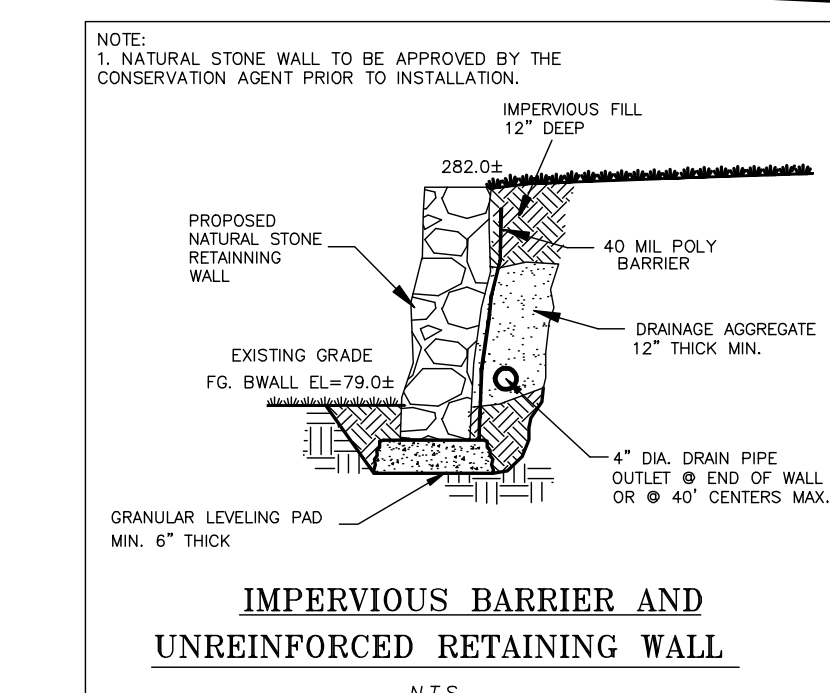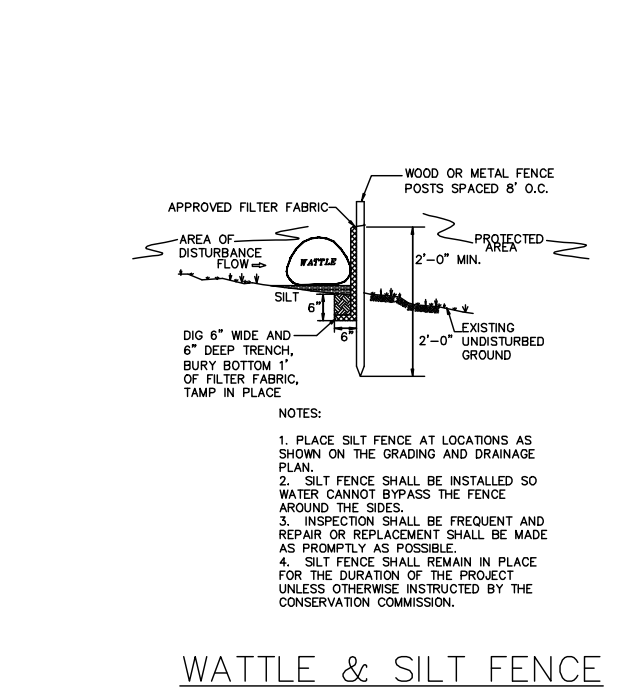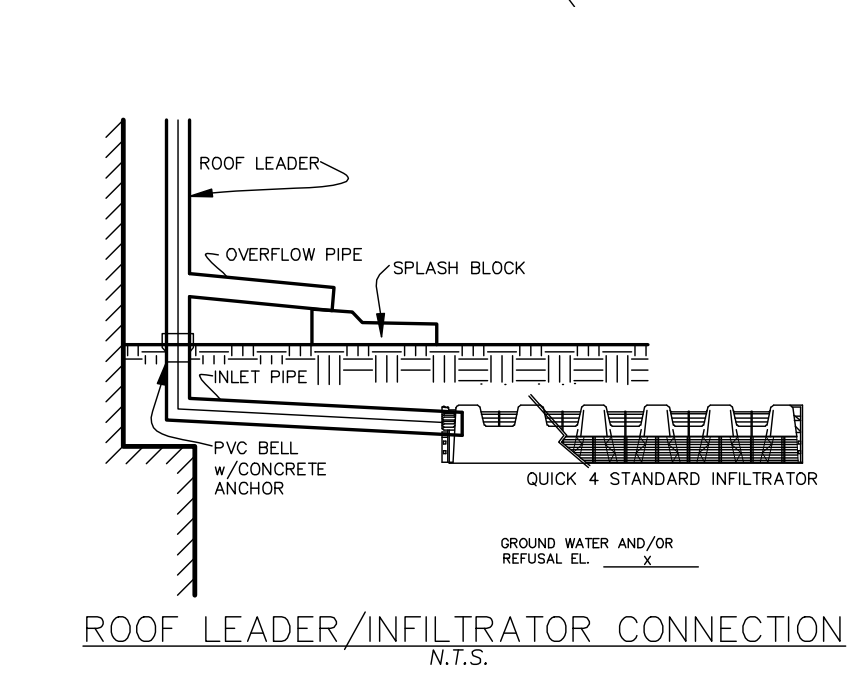

PLANT SCHEDULE

QUANTITY	COMMON NAME	BOTANICAL NAME	SYM.
4	RED-STEM DOGWOOD	CORNUS SERICEA	
9	INKBERRY	ILEX GLABRA	
5	ARROW-WOOD	VIURNUM RECUNITUM	

LOAM & WILD FLOWER SEED/MULCH

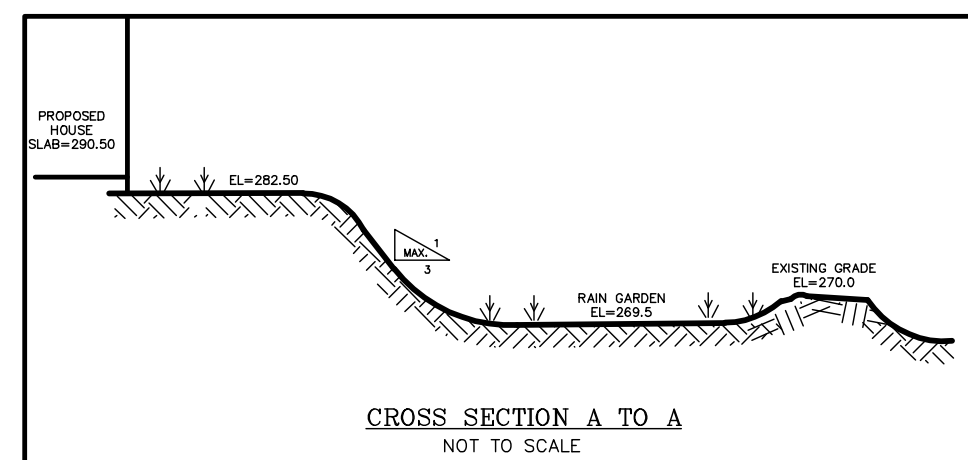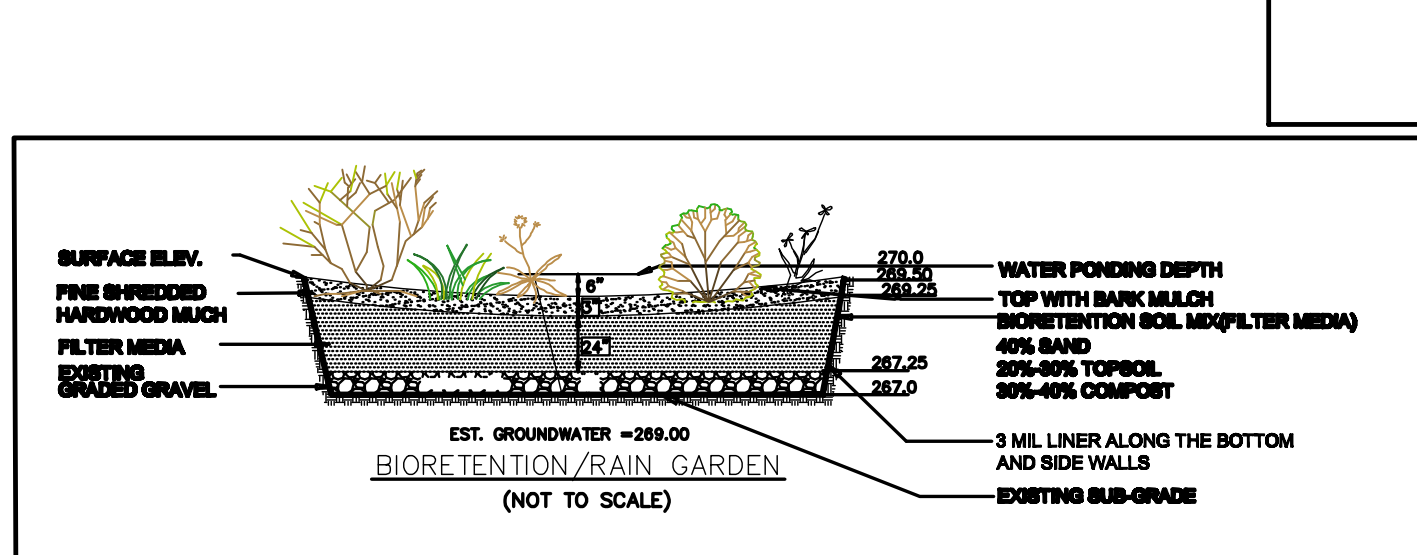

RESOURCE AREA PLAN
FOR
54 NEPONSET HEIGHTS AVENUE
IN
FOXBOROUGH, MA
SCALE: 10 FEET TO AN INCH
DATE: JULY 5, 2020

Landmark Site Design
Civil Engineering & Land Surveying
1267 GLEBE STREET, TAUNTON MA 02780
(774-265-0851
www.plavoie69@gmail.com
